HARKER HEIGHTS 2021 STREET IMPROVEMENTS - 277 CAL DAYS | BASIC LSGM | Feb-01-22 14:57

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors
HH 2021-WKD HARKER HEIGHTS 2021 STREET IMPROVEMENTS - 277 CAL DA		197	Dec-01-21	Sep-01-22		
HH 2021-WKD.1 PRECONSTRUCTION		5	Dec-01-21	Dec-07-21		
LSGM1000	NOTICE TO PROCEED	0	Dec-01-21*			LSGM1010, A1
LSGM1010	BOND	5	Dec-01-21	Dec-07-21	LSGM1000	LSGM1020
LSGM1020	TEXAS 811 DIG LOCATES	5	Dec-01-21	Dec-07-21	LSGM1010	LSGM1110
HH 2021-WKD.3 LONG LEAD ITEMS		86	Dec-01-21	Feb-24-22		
A1000	SLIPNOT SIDEWALK PLATE - NOLAN RUTH & OLD NOLANVILLE	52	Dec-01-21	Jan-21-22	LSGM1000	LSGM1190
A1010	SLIPNOT SIDEWALK PLATE - WILDEWOOD	52	Dec-01-21	Jan-21-22	LSGM1000	LSGM1830
A1020	RCB'S - WILDEWOOD	30	Dec-01-21	Dec-30-21	LSGM1000	LSGM1458
A1030	SET'S & RCP'S - WILDEWOOD	86	Dec-01-21	Feb-24-22	LSGM1000	LSGM1460
HH 2021-WKD.1000 PART J - NOLA RUTH/OLD NVILLE RD SW		15	Feb-21-22	Mar-11-22		
HH 2021-WKD.1000.1001 MOBILIZATION-9		1	Feb-21-22	Feb-21-22		
LSGM1110	EQUIPMENT TRANSPORT	1	Feb-21-22*	Feb-21-22	LSGM1020	LSGM1220
HH 2021-WKD.1000.1011 IMPLEMENT TCP-9		1	Feb-22-22	Feb-22-22		
LSGM1220	TRAFFIC CONTROL	1	Feb-22-22	Feb-22-22	LSGM1110	LSGM1130
HH 2021-WKD.1000.1003 CONSTRUCT SIDEWALK		9	Feb-23-22	Mar-07-22		
LSGM1130	SIDEWALK PLACEMENT	9	Feb-23-22	Mar-07-22	LSGM1220	LSGM1160
HH 2021-WKD.1000.1007 THREE 1' WIDE CONC PIERS CLASS A		2	Mar-08-22	Mar-09-22		
LSGM1160	PIERS PLACEMENT	2	Mar-08-22	Mar-09-22	LSGM1130	LSGM1190
HH 2021-WKD.1000.1009 MORTARED RIVER ROCK		2	Mar-10-22	Mar-11-22		
LSGM1190	INSTALL RIP RAP	2	Mar-10-22	Mar-11-22	LSGM1160,	LSGM2990
HH 2021-WKD.900 PART I - INDIAN TRAIL DRAINAGE		25	Mar-11-22	Apr-14-22		
HH 2021-WKD.900.901 MOBILIZATION-8		1	Mar-11-22	Mar-11-22		
LSGM2990	EQUIPMENT TRANSPORT	1	Mar-11-22	Mar-11-22	LSGM1190	LSGM3230
HH 2021-WKD.900.921 IMPLEMENT TCP-8		1	Mar-14-22	Mar-14-22		
LSGM3230	TRAFFIC CONTROL	1	Mar-14-22	Mar-14-22	LSGM2990	LSGM3020
HH 2021-WKD.900.903 PVC INSTALL		11	Mar-15-22	Mar-29-22		
LSGM3020	INSTALL PVC PIPE	11	Mar-15-22	Mar-29-22	LSGM3230	LSGM3100
HH 2021-WKD.900.910 CONCRETE		6	Mar-30-22	Apr-06-22		
LSGM3100	CONCRETE WORK	6	Mar-30-22	Apr-06-22	LSGM3020	LSGM3120
HH 2021-WKD.900.912 35 LF TRENCH DRAIN & GRATE		2	Apr-07-22	Apr-08-22		
LSGM3120	TRENCH DRAIN	2	Apr-07-22	Apr-08-22	LSGM3100	LSGM3110
HH 2021-WKD.900.911 ASPHALT TRENCH REPAIR		2	Apr-11-22	Apr-12-22		
LSGM3110	HMAC	2	Apr-11-22	Apr-12-22	LSGM3120	LSGM3170, LS
HH 2021-WKD.900.915 STRIPING & SIGNAGE		1	Apr-13-22	Apr-13-22		
LSGM3170	STRIPING & SIGNAGE	1	Apr-13-22	Apr-13-22	LSGM3110	LSGM3180
HH 2021-WKD.900.916 REVEGETATE DIST AREAS SEED/SOD/WATERING		1	Apr-14-22	Apr-14-22		
LSGM3180	SOD	1	Apr-14-22	Apr-14-22	LSGM3170	
HH 2021-WKD.600 PART F - POINT REPAIRS		14	Apr-07-22	Apr-26-22		
HH 2021-WKD.600.601 MOBILIZATION-5		1	Apr-07-22	Apr-07-22		
LSGM2600	EQUIPMENT TRANSPORT	1	Apr-07-22	Apr-07-22	LSGM3110	LSGM2620
HH 2021-WKD.600.603 IMPLEMENT TCP-5		1	Apr-08-22	Apr-08-22		
LSGM2620	TRAFFIC CONTROL	1	Apr-08-22	Apr-08-22	LSGM2600	LSGM2630
HH 2021-WKD.600.604 IMPLEMENT SWPPP-5		1	Apr-11-22	Apr-11-22		
LSGM2630	SWPPP	1	Apr-11-22	Apr-11-22	LSGM2620	LSGM2650
HH 2021-WKD.600.606 SAWCUT EXISTING ASPHALT-5		1	Apr-12-22	Apr-12-22		
LSGM2650	SAWCUT HMAC	1	Apr-12-22	Apr-12-22	LSGM2630	LSGM2660
HH 2021-WKD.600.607 UNCLASSIFIED EXCAVATION INCL ASPH/CLBM/SG		5	Apr-13-22	Apr-19-22		
LSGM2660	HMAC	5	Apr-13-22	Apr-19-22	LSGM2650	LSGM2670
HH 2021-WKD.600.608 6" TYPE B HMAC		2	Apr-20-22	Apr-21-22		
LSGM2670	HMAC	2	Apr-20-22	Apr-21-22	LSGM2660	LSGM2680
HH 2021-WKD.600.609 2" TYPE D HMAC		2	Apr-22-22	Apr-25-22		
LSGM2680	HMAC	2	Apr-22-22	Apr-25-22	LSGM2670	LSGM2690
HH 2021-WKD.600.610 STRIPING & SIGNAGE		1	Apr-26-22	Apr-26-22		
LSGM2690	STRIPING & SIGNAGE	1	Apr-26-22	Apr-26-22	LSGM2680	
HH 2021-WKD.200 PART B - CROWFOOT		23	Mar-07-22	Apr-06-22		
HH 2021-WKD.200.201 MOBILIZATION-1		1	Mar-07-22	Mar-07-22		
LSGM1950	EQUIPMENT TRANSPORT	1	Mar-07-22*	Mar-07-22		LSGM1970
HH 2021-WKD.200.203 IMPLEMENT TCP-1		1	Mar-07-22	Mar-07-22		
LSGM1970	TRAFFIC CONTROL	1	Mar-07-22	Mar-07-22	LSGM1950	LSGM1980

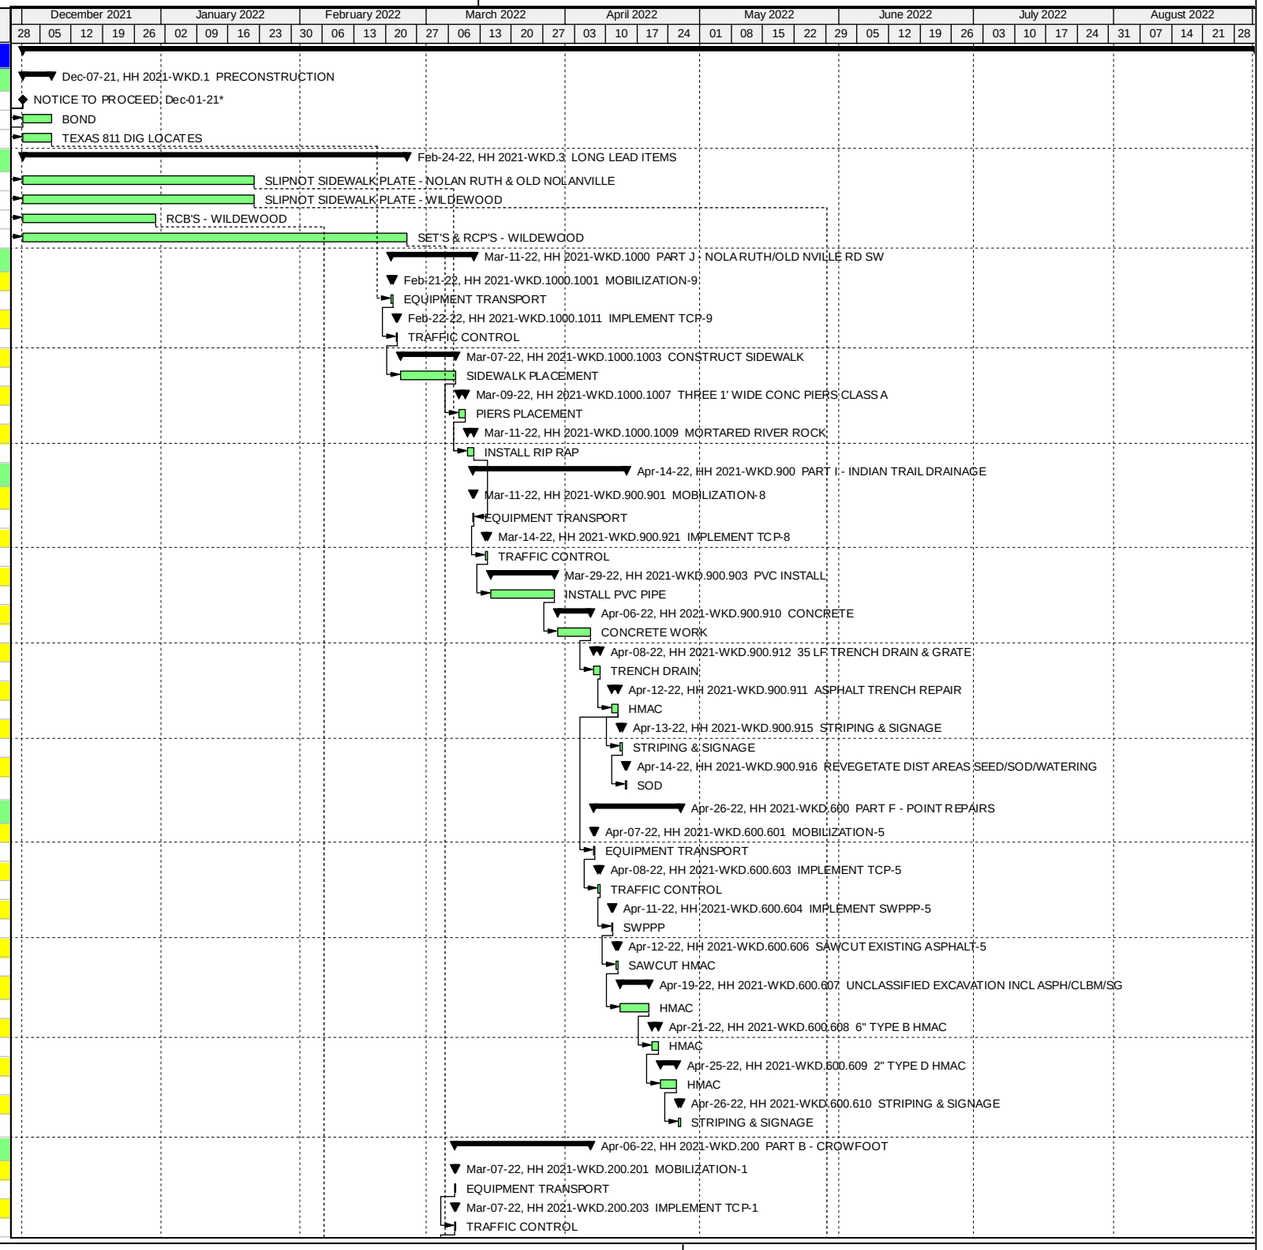

© Oracle Corporation

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors
HH 2021-WKD.200.204 IMPLEMENT SWPPP-1		1	Mar-07-22	Mar-07-22		
LSGM1980	SWPPP	1	Mar-07-22	Mar-07-22	LSGM1970	LSGM2010
HH 2021-WKD.200.207 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY-1		17	Mar-08-22	Mar-30-22		
LSGM2010	CEMENT TREATED BASE	17	Mar-08-22	Mar-30-22	LSGM1980	LSGM2040
HH 2021-WKD.200.209 2.5" TYPE D HMAC-1		3	Mar-31-22	Apr-04-22		
LSGM2040	HMAC	3	Mar-31-22	Apr-04-22	LSGM2010	LSGM2050, LS
HH 2021-WKD.200.210 STRIPING & SIGNAGE		2	Apr-05-22	Apr-06-22		
LSGM2050	STRIPING & SIGNAGE	2	Apr-05-22	Apr-06-22	LSGM2040	
HH 2021-WKD.700 PART G - MEMORY/SHELBY		20	Apr-01-22	Apr-28-22		
HH 2021-WKD.700.701 MOBILIZATION-6		1	Apr-01-22	Apr-01-22		
LSGM2720	SITE MOBILIZATION	1	Apr-01-22	Apr-01-22	LSGM2040	LSGM2730, A1
HH 2021-WKD.700.703 IMPLEMENT TCP-6		1	Apr-04-22	Apr-04-22		
LSGM2730	TRAFFIC CONTROL	1	Apr-04-22	Apr-04-22	LSGM2720	LSGM2740
HH 2021-WKD.700.704 IMPLEMENT SWPPP-6		1	Apr-05-22	Apr-05-22		
LSGM2740	SWPPP	1	Apr-05-22	Apr-05-22	LSGM2730	LSGM2760
HH 2021-WKD.700.712 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY-5		13	Apr-06-22	Apr-22-22		
LSGM2760	CEMENT TREATED BASE	13	Apr-06-22	Apr-22-22	LSGM2740	LSGM2790
HH 2021-WKD.700.714 2.5" TYPE D HMAC-5		2	Apr-25-22	Apr-26-22		
LSGM2790	HMAC	2	Apr-25-22	Apr-26-22	LSGM2760	LSGM2800, LS
HH 2021-WKD.700.715 STRIPING & SIGNAGE		2	Apr-27-22	Apr-28-22		
LSGM2800	STRIPING & SIGNAGE	2	Apr-27-22	Apr-28-22	LSGM2790	
HH 2021-WKD.HH 2021-WKD.701 MEMORY LANE KNUCKLE REMOVAL		9	Apr-04-22	Apr-14-22		
HH 2021-WKD.HH 2021-WKD.701.1 REMOVE/DISPOSE EXISTING CURB AND GUTTER		1	Apr-04-22	Apr-04-22		
A1040	REMOVE/DISPOSE EXISTING CURB AND GUTTER	1	Apr-04-22	Apr-04-22	LSGM2720	A1050
HH 2021-WKD.HH 2021-WKD.701.2 UNCLASSIFIED EXCAVATION (ASPHALT/BASE 6" DEPTH)		2	Apr-05-22	Apr-06-22		
A1050	UNCLASSIFIED EXCAVATION (ASPHALT/BASE 6" DEPTH)	2	Apr-05-22	Apr-06-22	A1040	A1060
HH 2021-WKD.HH 2021-WKD.701.3 INSTALL CURB & GUTTER		3	Apr-07-22	Apr-11-22		
A1060	INSTALL CURB & GUTTER	3	Apr-07-22	Apr-11-22	A1050	A1070
HH 2021-WKD.HH 2021-WKD.701.4 SAWCUT EXISTING ASPHALT		1	Apr-12-22	Apr-12-22		
A1070	SAWCUT EXISTING ASPHALT	1	Apr-12-22	Apr-12-22	A1060	A1080
HH 2021-WKD.HH 2021-WKD.701.5 FURNISH & INSTALL TOPSOIL (6" DEPTH)		1	Apr-13-22	Apr-13-22		
A1080	FURNISH & INSTALL TOPSOIL (6" DEPTH)	1	Apr-13-22	Apr-13-22	A1070	A1090
HH 2021-WKD.HH 2021-WKD.701.6 FURNISH & INSTALL SOD, INCL WATERING TO EST GROWTH		1	Apr-14-22	Apr-14-22		
A1090	FURNISH & INSTALL SOD, INCL WATERING TO EST GROWTH	1	Apr-14-22	Apr-14-22	A1080	
HH 2021-WKD.300 PART C - MILLER'S CROSSING		11	Apr-25-22	May-09-22		
HH 2021-WKD.300.301 MOBILIZATION-2		1	Apr-25-22	Apr-25-22		
LSGM2100	EQUIPMENT TRANSPORT	1	Apr-25-22	Apr-25-22	LSGM2790	LSGM2120
HH 2021-WKD.300.303 IMPLEMENT TCP-2		1	Apr-25-22	Apr-25-22		
LSGM2120	TRAFFIC CONTROL	1	Apr-25-22	Apr-25-22	LSGM2100	LSGM2130
HH 2021-WKD.300.304 IMPLEMENT SWPPP-2		1	Apr-25-22	Apr-25-22		
LSGM2130	SWPPP	1	Apr-25-22	Apr-25-22	LSGM2120	LSGM2160
HH 2021-WKD.300.307 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY-2		7	Apr-25-22	May-03-22		
LSGM2160	CEMENT TREATED BASE	7	Apr-25-22	May-03-22	LSGM2130	LSGM2200
HH 2021-WKD.300.310 ASPH/CONC INTERFACE REPAIR		2	May-04-22	May-05-22		
LSGM2200	HMAC	2	May-04-22	May-05-22	LSGM2160	LSGM2190
HH 2021-WKD.300.309 2.5" TYPE D HMAC-2		2	May-04-22	May-05-22		
LSGM2190	HMAC	2	May-04-22	May-05-22	LSGM2200	LSGM2210, LS
HH 2021-WKD.300.311 STRIPING & SIGNAGE		2	May-06-22	May-09-22		
LSGM2210	STRIPING & SIGNAGE	2	May-06-22	May-09-22	LSGM2190	
HH 2021-WKD.399 PART D - PIONEER TRAIL.		16	May-04-22	May-25-22		
HH 2021-WKD.399.401 MOBILIZATION-3		1	May-04-22	May-04-22		
LSGM2270	EQUIPMENT TRANSPORT	1	May-04-22	May-04-22	LSGM2190	LSGM2290
HH 2021-WKD.399.403 IMPLEMENT TCP-3		1	May-04-22	May-04-22		
LSGM2290	TRAFFIC CONTROL	1	May-04-22	May-04-22	LSGM2270	LSGM2300
HH 2021-WKD.399.404 IMPLEMENT SWPPP-3		1	May-04-22	May-04-22		
LSGM2300	SWPPP	1	May-04-22	May-04-22	LSGM2290	LSGM2330
HH 2021-WKD.399.407 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY-3		11	May-04-22	May-18-22		
LSGM2330	CEMENT TREATED BASE	11	May-04-22	May-18-22	LSGM2300	LSGM2370
HH 2021-WKD.399.410 ADJUST EX MANHOLE		1	May-19-22	May-19-22		
LSGM2370	ADJUST MANHOLES	1	May-19-22	May-19-22	LSGM2330	LSGM2360
HH 2021-WKD.399.409 2.5" TYPE D HMAC-3		2	May-20-22	May-23-22		

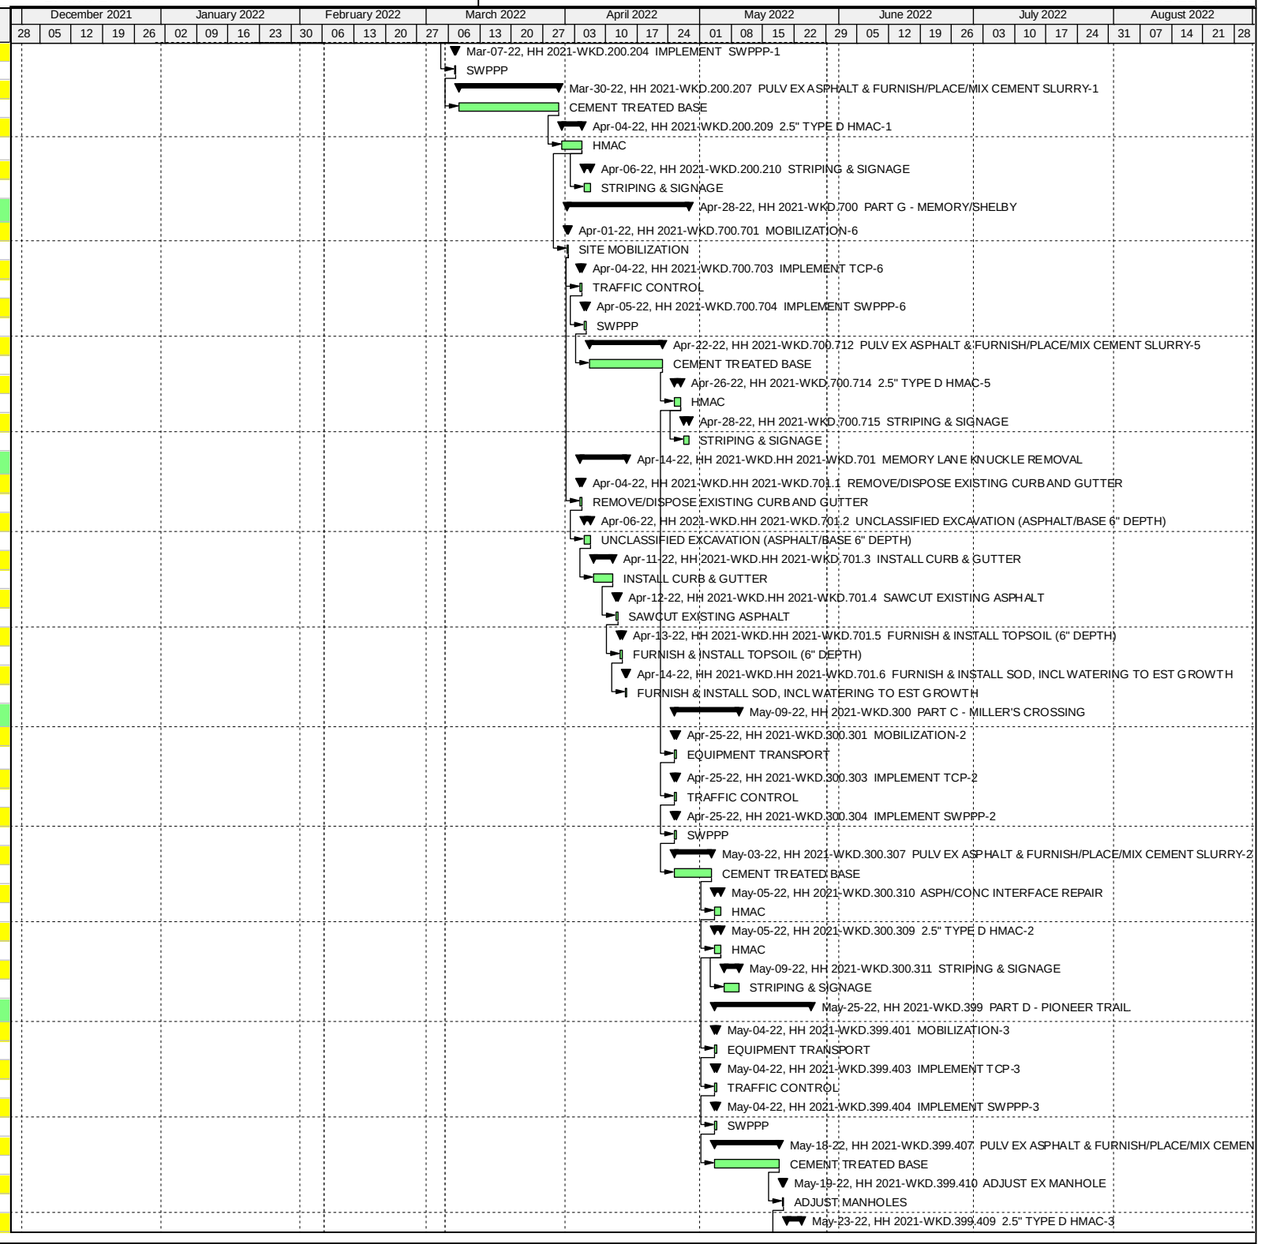

CITY OF HARKER HEIGHTS, TEXAS
2021 STREET IMPROVEMENTS
NTP DATE: 12/01/2021
277 CALENDER DAYS FROM NTP (Incl. C/O #01)

TASK filter: All Activities

© Oracle Corporation

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors
LSGM2360	HMAC	2	May-20-22	May-23-22	LSGM2370	LSGM2380, LS
HH 2021-WKD.399.411 STRIPING & SIGNAGE		2	May-24-22	May-25-22		
LSGM2380	STRIPING & SIGNAGE	2	May-24-22	May-25-22	LSGM2360	
HH 2021-WKD.800 PART H - DRAWBRIDGE/COMANCHE GAP		18	May-20-22	Jun-14-22		
HH 2021-WKD.800.801 MOBILIZATION-7		0	May-20-22	May-20-22		
LSGM2860	SITE MOBILIZATION	0	May-20-22		LSGM2360	LSGM2870
HH 2021-WKD.800.803 IMPLEMENT TCP-7		1	May-20-22	May-20-22		
LSGM2870	TRAFFIC CONTROL	1	May-20-22	May-20-22	LSGM2860	LSGM2880
HH 2021-WKD.800.804 IMPLEMENT SWPPP-7		1	May-23-22	May-23-22		
LSGM2880	SWPPP	1	May-23-22	May-23-22	LSGM2870	LSGM2900
HH 2021-WKD.800.812 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY-6		12	May-24-22	Jun-08-22		
LSGM2900	CEMENT TREADED BASE	12	May-24-22	Jun-08-22	LSGM2880	LSGM2930
HH 2021-WKD.800.814 1.5" TYPE D HMAC		2	Jun-09-22	Jun-10-22		
LSGM2930	HMAC	2	Jun-09-22	Jun-10-22	LSGM2900	LSGM2940
HH 2021-WKD.800.815 2.5" TYPE D HMAC-6		1	Jun-13-22	Jun-13-22		
LSGM2940	HMAC	1	Jun-13-22	Jun-13-22	LSGM2930	LSGM2950, LS
HH 2021-WKD.800.816 STRIPING & SIGNAGE		1	Jun-14-22	Jun-14-22		
LSGM2950	STRIPING & SIGNAGE	1	Jun-14-22	Jun-14-22	LSGM2940	
HH 2021-WKD.100 PART A - CHAUCER		23	Jun-08-22	Jul-08-22		
HH 2021-WKD.100.101 MOBILIZATION		1	Jun-10-22	Jun-10-22		
LSGM1200	EQUIPMENT TRANSPORT	1	Jun-10-22	Jun-10-22	LSGM2940	LSGM1230
HH 2021-WKD.100.103 IMPLEMENT TCP		1	Jun-10-22	Jun-10-22		
LSGM1230	TRAFFIC CONTROL	1	Jun-10-22	Jun-10-22	LSGM1200	LSGM1240
HH 2021-WKD.100.104 IMPLEMENT SWPPP		1	Jun-10-22	Jun-10-22		
LSGM1240	SWPPP	1	Jun-10-22	Jun-10-22	LSGM1230	LSGM1270
HH 2021-WKD.100.107 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY		18	Jun-08-22	Jul-01-22		
LSGM1270	CEMENT TREATED BASE	18	Jun-08-22	Jul-01-22	LSGM1240	LSGM1300
HH 2021-WKD.100.109 2.5" TYPE D HMAC		3	Jul-04-22	Jul-06-22		
LSGM1300	HMAC	3	Jul-04-22	Jul-06-22	LSGM1270	LSGM1330
HH 2021-WKD.100.110 STRIPING & SIGNAGE		2	Jul-07-22	Jul-08-22		
LSGM1330	STRIPING & SIGNAGE	2	Jul-07-22	Jul-08-22	LSGM1300	
HH 2021-WKD.1100 PART K - WILDEWOOD DRAINAGE		129	Dec-06-21	Jun-02-22		
HH 2021-WKD.1100.1101 MOBILIZATION-10		1	Dec-06-21	Dec-06-21		
LSGM1310	EQUIPMENT TRANSPORT	1	Dec-06-21*	Dec-06-21		LSGM1340
HH 2021-WKD.1100.1102 PREP ROW		4	Dec-06-21	Dec-09-21		
LSGM1340	PREP ROW	4	Dec-06-21	Dec-09-21	LSGM1310	LSGM1380
HH 2021-WKD.1100.1106 IMPLEMENT TCP-10		1	Dec-10-21	Dec-10-21		
LSGM1380	TRAFFIC CONTROL	1	Dec-10-21	Dec-10-21	LSGM1340	LSGM1390
HH 2021-WKD.1100.1107 PREPARE SWPPP		1	Dec-10-21	Dec-10-21		
LSGM1390	SWPPP	1	Dec-10-21	Dec-10-21	LSGM1380	LSGM1410
HH 2021-WKD.1100.1109 DEMOLITION		42	Dec-13-21	Feb-08-22		
LSGM1410	DEMOLITION WORK	12	Dec-13-21	Dec-28-21	LSGM1390	LSGM1420
LSGM1420	REPAIR 12" GRAVITY SEWER LINE	30	Dec-29-21*	Feb-08-22	LSGM1410	LSGM1458
HH 2021-WKD.1100.1114 STORM DRAINAGE		64	Feb-09-22	May-09-22		
LSGM1458	INSTALL RCB/HEADWALLS	19	Feb-09-22	Mar-07-22	A1020, LSG	LSGM1460
LSGM1460	STORM DRAINAGE INSTALLATION	45	Mar-08-22	May-09-22	A1030, LSG	LSGM1740
HH 2021-WKD.1100.1133 6" CONC DRIVEWAYS 3,000 PSI		4	May-10-22	May-13-22		
LSGM1740	DRIVEWAY PATCHES	4	May-10-22	May-13-22	LSGM1460	LSGM1750, LS
HH 2021-WKD.1100.1134 ASPHALT TRENCH REPAIR-1		2	May-16-22	May-17-22		
LSGM1750	HMAC	2	May-16-22	May-17-22	LSGM1740	
HH 2021-WKD.1100.1135 MINOR SWALE GRADING		2	May-16-22	May-17-22		
LSGM1760	FINE GRADE	2	May-16-22	May-17-22	LSGM1740	LSGM1780
HH 2021-WKD.1100.1137 CONSTRUCT SIDEWALK		10	May-18-22	May-31-22		
LSGM1780	SIDEWALK INSTALLATION	10	May-18-22	May-31-22	LSGM1760	LSGM1830
HH 2021-WKD.1100.1142 PEDESTRIAN HANDRAIL TYPE B-1		1	Jun-01-22	Jun-01-22		
LSGM1830	HANDRAIL	1	Jun-01-22	Jun-01-22	LSGM1780,	LSGM1770
HH 2021-WKD.1100.1136 REVEGETATE DIST AREAS SEED/SOD/WATERING-1		1	Jun-02-22	Jun-02-22		
LSGM1770	HYDROMULCH FLEXTERRA	1	Jun-02-22	Jun-02-22	LSGM1830	LSGM2410
HH 2021-WKD.500 PART E - WILDEWOOD DRIVE		49	Jun-03-22	Aug-10-22		
HH 2021-WKD.500.501 MOBILIZATION-4		1	Jun-03-22	Jun-03-22		
LSGM2410	EQUIPMENT TRANSPORT	1	Jun-03-22	Jun-03-22	LSGM1770	LSGM2430

CITY OF HARKER HEIGHTS, TEXAS
2021 STREET IMPROVEMENTS
NTP DATE: 12/01/2021
277 CALENDER DAYS FROM NTP (Incl. C/O #01)

TASK filter: All Activities

© Oracle Corporation

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- summary

HARKER HEIGHTS 2021 STREET IMPROVEMENTS - 277 CAL DAYS | BASIC LSGM | Feb-01-22 14:57

Activity ID	Activity Name	Original Duration	Start	Finish	Predecessors	Successors
HH 2021-WKD.500.503 IMPLEMENT TCP-4		1	Jun-06-22	Jun-06-22		
LSGM2430	TRAFFIC CONTROL	1	Jun-06-22	Jun-06-22	LSGM2410	LSGM2440
HH 2021-WKD.500.504 IMPLEMENT SWPPP-4		1	Jun-07-22	Jun-07-22		
LSGM2440	SWPPP	1	Jun-07-22	Jun-07-22	LSGM2430	LSGM2470
HH 2021-WKD.500.507 CONSTRUCT CURB		20	Jun-08-22	Jul-05-22		
LSGM2470	CURB INSTALLATION	20	Jun-08-22	Jul-05-22	LSGM2440	LSGM2520
HH 2021-WKD.500.512 PULV EX ASPHALT & FURNISH/PLACE/MIX CEMENT SLURRY-4		20	Jul-06-22	Aug-02-22		
LSGM2520	CEMENT TREATED BASE	20	Jul-06-22	Aug-02-22	LSGM2470	LSGM2560
HH 2021-WKD.500.515 ADJUST EX MANHOLE-1		1	Aug-03-22	Aug-03-22		
LSGM2560	ADJUST MANHOLE	1	Aug-03-22	Aug-03-22	LSGM2520	LSGM2550
HH 2021-WKD.500.514 2.5" TYPE D HMAC-4		3	Aug-04-22	Aug-08-22		
LSGM2550	HMAC	3	Aug-04-22	Aug-08-22	LSGM2560	LSGM2570
HH 2021-WKD.500.516 STRIPING & SIGNAGE		2	Aug-09-22	Aug-10-22		
LSGM2570	STRIPING & SIGNAGE	2	Aug-09-22	Aug-10-22	LSGM2550	LSGM1040
HH 2021-WKD.2 CLOSEOUT		16	Aug-11-22	Sep-01-22		
LSGM1040	CONTRACTORS GENERATED PUNCHLIST	1	Aug-11-22	Aug-11-22	LSGM2570	LSGM1050
LSGM1050	CONTRACTOR PUNCHLIST CORRECTIONS	5	Aug-12-22	Aug-18-22	LSGM1040	LSGM1060
LSGM1060	PREFINAL INSPECTION	1	Aug-19-22	Aug-19-22	LSGM1050	LSGM1070
LSGM1070	PREFINAL INSPECTION CORRECTIONS	5	Aug-22-22	Aug-26-22	LSGM1060	LSGM1080
LSGM1080	FINAL INSPECTION	1	Aug-29-22	Aug-29-22	LSGM1070	LSGM1090
LSGM1090	CLOSEOUT DOCUMENTS	3	Aug-30-22	Sep-01-22	LSGM1080	LSGM1100
LSGM1100	PROJECT COMPLETION (277 CALDAYS FROM NTP)	0		Sep-01-22*	LSGM1090	

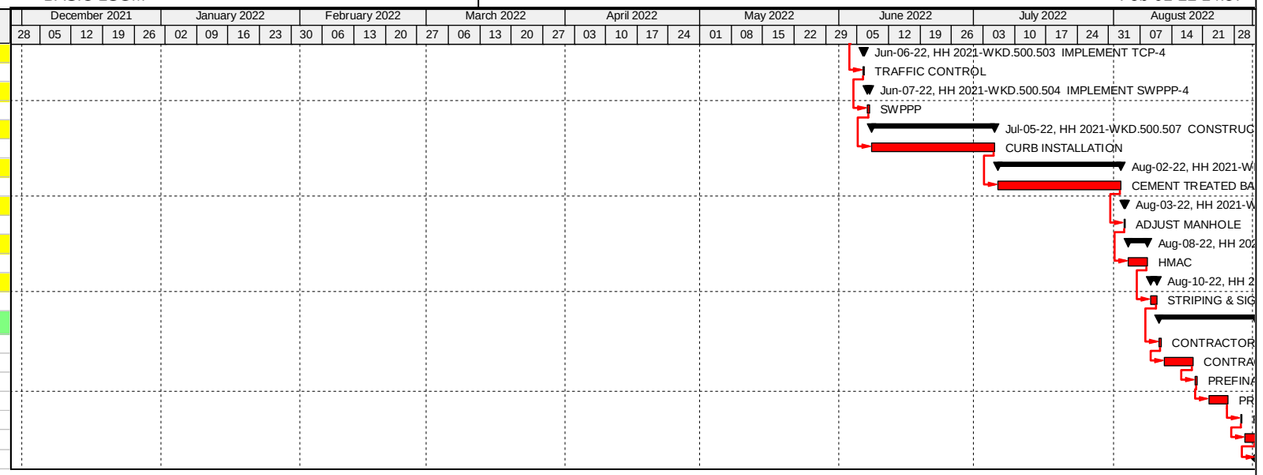

Dylan Morphet

Digitally signed by Dylan Morphet
DN: C=US, E=dylan.morphet@lonestargrading.com, O=Lone Star Grading and Materials, OU=Project Manager, CN=Dylan Morphet
Date: 2022.02.01 17:03:42-06'00'

© Oracle Corporation

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- summary
